


Scheme Update – November 2020

Scheme Progress



Visit our website to see the latest video drone footage of the scheme

Introduction

Over the last month we have made significant progress with the installation of the beams, the 800 tonne crane has already installed the beams over the river Sow, the remaining beams are planned to be installed by the end of the month.



What are we doing now?


The new road Unicorn Way is progressing well, we are finalising the footpaths along with the signage and street lighting, surfacing works will commence by the end of November with a view to opening this section of road in the New Year.

Madford Retail Park pedestrian diversion is scheduled to be removed by the end of November and the original pedestrian route reinstated. We are continuing to progress with the earth filled retaining wall works and drainage between Lidl and Tenpin.

Works along Doxey Road are progressing well, the new toucan crossing is installed and scheduled to go live by the end of November.

Our next significant milestone of works is on the Doxey Road railway bridge, there will be a new road alignment and surfacing over the bridge, in order to carry out these works the bridge will be closed to vehicles, pedestrian and cycle access will be maintained throughout. Vehicular traffic will be diverted along the new Unicorn Way and via Martin Drive. The closure is scheduled from mid-January until Mid-June, full details of this phase of works will be made available and issued in December.

Key Milestones

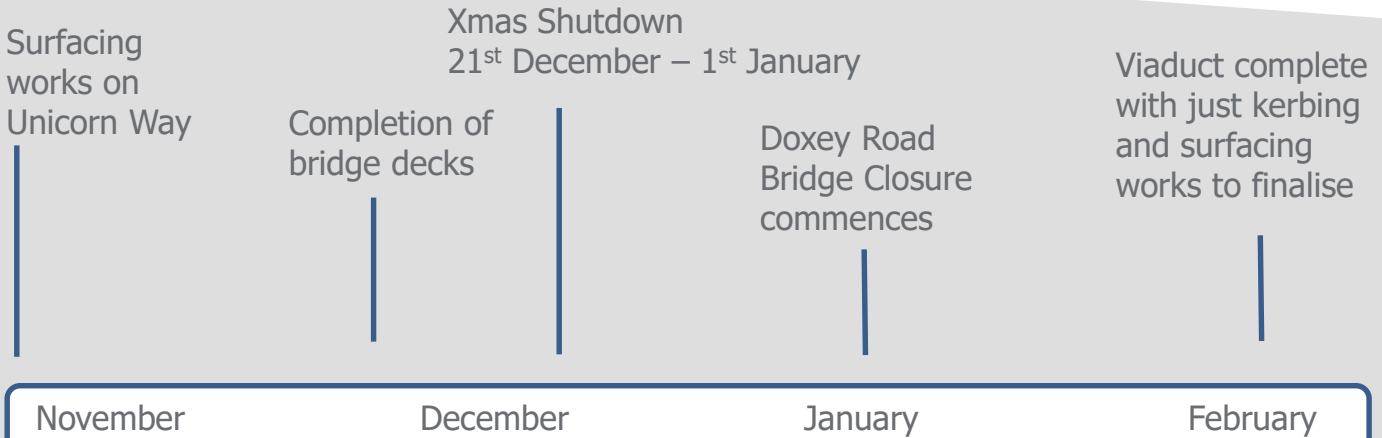

*Dates in accordance with current programme and could be subject to change
